ID	% Complete	Task Name	Duration (work days)	Start	Finish
1	100%	BLM Select Third-party Contractor	41 days	Mon 7/31/06	Tue 9/26/06
2	100%	**Golder Task 01 - Develop LUA/EIS Project Management Plan**	**67 days**	**Mon 10/2/06**	**Fri 1/19/07**
17	100%	**Golder Task 02 - Provide Scoping Process Support**	**63 days**	**Fri 10/13/06**	**Fri 1/26/07**
28	80%	**Golder Task 03 - Develop Analysis of the Management Situation**	**570 days**	**Mon 10/9/06**	**Tue 1/27/09**
60	75%	**Golder Task 04 - Develop Draft LUA/Draft EIS**	**274 days**	**Fri 8/24/07**	**Wed 9/24/08**
61	100%	Subtask 4.1 Develop Admin Draft LUA/Admin Draft EIS (ADLUA/ADEIS)	52 days	Fri 8/24/07	Wed 11/7/07
62	*100%*	*BLM Review ADLUA/ADEIS (coinciding review by BLM-WO and DOI)*	*23 days*	*Thu 11/8/07*	*Tue 12/11/07*
63	**100%**	**Subtask 4.2.1 Develop Draft LUA/Draft EIS (DLUA/DEIS)**	**50 days**	**Wed 12/12/07**	**Mon 2/25/08**
64	***100%***	***BLM Review DLUA/DEIS***	***17 days***	***Tue 2/26/08***	***Wed 3/19/08***
65	**100%**	**Subtask 4.2.2 Develop Camera-ready Internet-ready DLUA/DEIS**	**6 days**	**Thu 3/20/08**	**Thu 3/27/08**
66	0%	*BLM Submit Notice of Availability of DLUA/DEIS in Federal Register*	5 days	Mon 6/16/08	Fri 6/20/08
67	***50%***	***EPA Submit Notice of Availability of DLUA/DEIS in Federal Register***	***5 days***	***Fri 6/27/08***	***Thu 7/3/08***
68	***100%***	***BLM Print and Distribute DLUA/DEIS***	***60 days***	***Mon 3/31/08***	***Mon 6/23/08***
69	***0%***	***Public Review of DLUA/DEIS 90 days***	***62 days***	***Fri 6/27/08***	***Wed 9/24/08***
70	**0%**	**Golder Task 05 - Solicit Public Comment on the DLUA/DEIS**	**96 days**	**Mon 6/23/08**	**Thu 11/6/08**
71	**0%**	**Subtask 5.1.1 Develop Draft Public Hearing Materials**	**10 days**	**Mon 6/23/08**	**Mon 7/7/08**
72	***0%***	***BLM Review Draft Public Hearing Materials***	***10 days***	***Tue 7/8/08***	***Mon 7/21/08***
73	**0%**	**Subtask 5.1.2 Develop Final Public Hearing Materials**	**5 days**	**Tue 7/22/08**	**Mon 7/28/08**
74	***0%***	***BLM Hold Public Hearing on DLUA/DEIS***	***3 days***	***Wed 7/30/08***	***Fri 8/1/08***
75	**0%**	**Subtask 5.2 Facilitate Public Hearing Open House**	**3 days**	**Wed 7/30/08**	**Fri 8/1/08**
76	**0%**	**Subtask 5.3.1 Develop Comment Database**	**10 days**	**Mon 7/7/08**	**Fri 7/18/08**
77	0%	Subtask 5.3.2 Develop Draft Comment Summary Report	10 days	Thu 9/25/08	Wed 10/8/08
78	*0%*	*BLM Review Draft Comment Summary Report*	*10 days*	*Thu 10/9/08*	*Thu 10/23/08*
79	0%	Subtask 5.3.3 Develop Final Comment Summary Report	5 days	Fri 10/24/08	Thu 10/30/08
80	0%	Subtask 5.4.1 Develop Draft Comment and Response Appendix	10 days	Thu 9/25/08	Wed 10/8/08
81	*0%*	*BLM Review Draft Comment and Response Appendix*	*10 days*	*Thu 10/9/08*	*Thu 10/23/08*
82	0%	Subtask 5.4.2 Develop Final Comment and Response Appendix	10 days	Fri 10/24/08	Thu 11/6/08

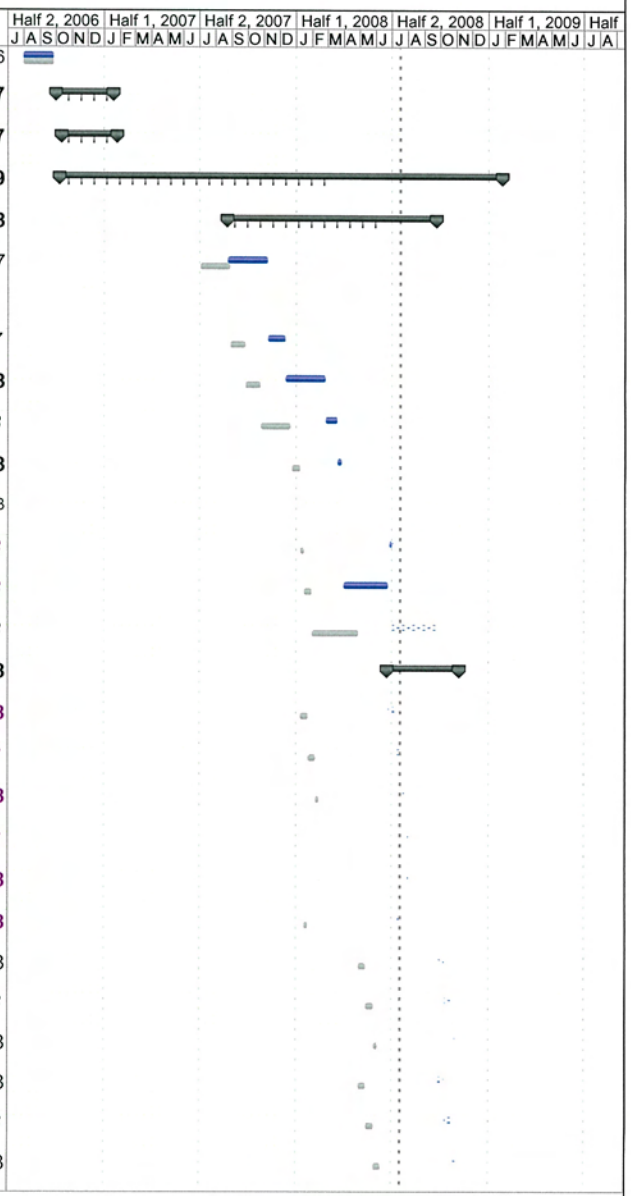

East Lynn Lake Coal Lease

Critical	Baseline	Project Summary	Baseline
Critical Split	Baseline Split	Critical Split	Baseline Split
Critical Progress	Baseline Milestone	Critical Progress	Baseline Milestone
Task	Milestone	Task	Milestone
Split	Summary Progress	Split	Summary Progress
Task Progress	Summary	Task Progress	Summary

ID	% Complete	Task Name	Duration (work days)	Start	Finish
83	100%	**Golder Task 06 - Perform Socioeconomic Analysis**	**275 days**	**Fri 2/16/07**	**Thu 3/20/08**
92	0%	**Golder Task 07 - Develop Proposed LUA/Final EIS (PLUA/FEIS)**	**107 days**	**Fri 11/7/08**	**Tue 4/14/09**
93	0%	Subtask 7.1 Develop Admin Prop. LUA/Admin Final EIS (APLUA/AFEIS)	30 days	Fri 11/7/08	Mon 12/22/08
94	*0%*	*BLM Review APLUA/AFEIS*	*20 days*	*Tue 12/23/08*	*Thu 1/22/09*
95	0%	Subtask 7.2 Develop Camera/Internet-ready Proposed LUA/Final EIS	10 days	Fri 1/23/09	Thu 2/5/09
96	*0%*	*BLM Submit Notice of Availability of the PLUA/FEIS in the Fed. Register*	*5 days*	*Fri 2/6/09*	*Thu 2/12/09*
97	*0%*	*BLM Print and Distribute PLUA/FEIS*	*5 days*	*Fri 2/6/09*	*Thu 2/12/09*
98	*0%*	*Public Protest Period PLUA/FEIS & Governor's Consistency Review*	*42 days*	*Fri 2/13/09*	*Tue 4/14/09*
99	0%	**Golder Task 08 - Develop Approved LUA/Record of Decision (ALUA/ROD)**	**75 days**	**Wed 3/18/09**	**Wed 7/1/09**
100	0%	Subtask 8.1 Assist in Response to Protests to PLUA/FEIS	15 days	Wed 3/18/09	Tue 4/7/09
101	0%	Subtask 8.2 Prepare Draft Summary of Resolution of Protests	10 days	Wed 4/8/09	Tue 4/21/09
102	*0%*	*BLM Review Draft Summary of Resolution of Protests*	*10 days*	*Wed 4/22/09*	*Tue 5/5/09*
103	0%	Subtask 8.3 Prepare Final Summary of Resolution of Protests	5 days	Wed 5/6/09	Tue 5/12/09
104	0%	Subtask 8.4 Prepare Draft ALUA/ROD	10 days	Wed 5/13/09	Wed 5/27/09
105	*0%*	*BLM Review of Draft ALUA/ROD*	*15 days*	*Thu 5/28/09*	*Wed 6/17/09*
106	0%	Subtask 8.5 Prepare Final ALUA/ROD	10 days	Thu 6/18/09	Wed 7/1/09
107	56%	**Golder Task 09 - Prepare Executive Summaries**	**317 days**	**Thu 11/1/07**	**Thu 2/5/09**
108	100%	Subtask 9.1 Prepare Executive Summary for ADLUA/ADEIS	5 days	Thu 11/1/07	Wed 11/7/07
109	*100%*	*BLM Review Executive Summary for ADLUA/ADEIS*	*23 days*	*Thu 11/8/07*	*Tue 12/11/07*
110	**100%**	Subtask 9.2 Prepare Executive Summary for DLUA/DEIS	**5 days**	**Fri 2/15/08**	**Mon 2/25/08**
111	***100%***	*BLM Review Executive Summary for DLUA/DEIS*	***17 days***	***Tue 2/26/08***	***Wed 3/19/08***
112	0%	Subtask 9.3 Prepare Executive Summary for APLUA/AFEIS	10 days	Fri 11/7/08	Fri 11/21/08
113	*0%*	*BLM Review Executive Summary for APLUA/AFEIS*	*20 days*	*Tue 12/23/08*	*Thu 1/22/09*
114	0%	Subtask 9.4 Prepare Executive Summary for PLUA/FEIS	10 days	Fri 1/23/09	Thu 2/5/09
115	8%	**Golder Task 10 - Provide External Affairs Support**	**730 days**	**Tue 8/1/06**	**Tue 7/7/09**
122	33%	**Golder Task 11 - Project Management**	**730 days**	**Tue 8/1/06**	**Tue 7/7/09**
123	33%	Subtask 11.1 - Prepare Progress Reports	730 days	Tue 8/1/06	Tue 7/7/09
124	33%	Subtask 11.2 - Perform Project Management	730 days	Tue 8/1/06	Tue 7/7/09

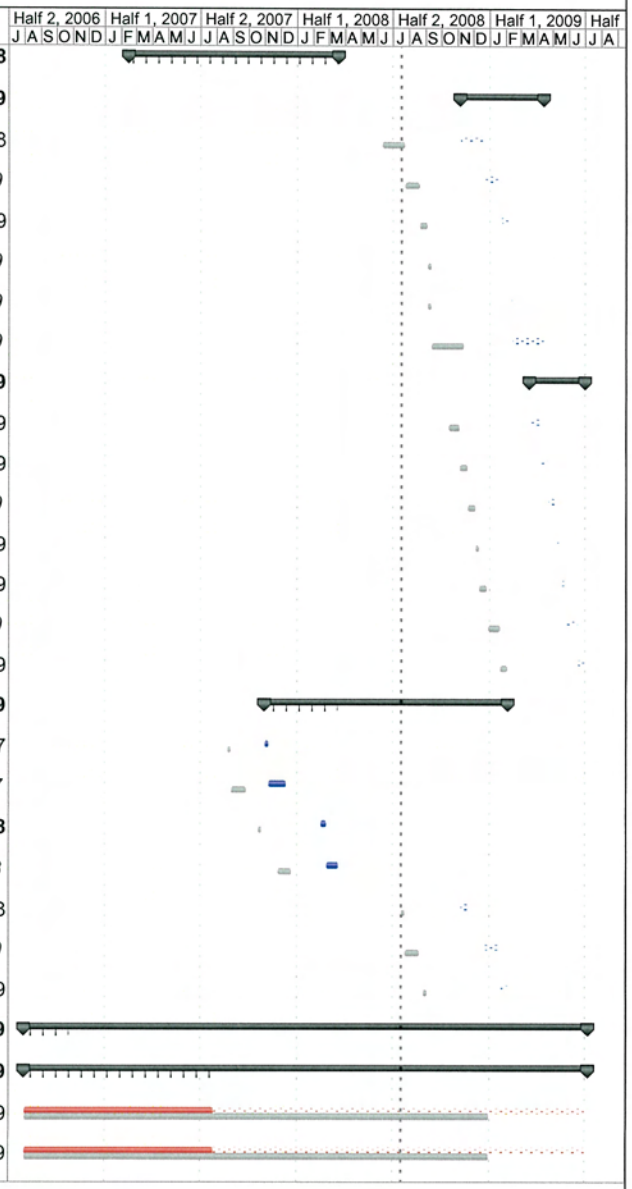

East Lynn Lake Coal Lease

Critical	Baseline	Project Summary	Baseline
Critical Split	Baseline Split	Critical Split	Baseline Split
Critical Progress	Baseline Milestone	Critical Progress	Baseline Milestone
Task	Milestone	Task	Milestone
Split	Summary Progress	Split	Summary Progress
Task Progress	Summary	Task Progress	Summary
